

# CITY OF BURNABY COMMUNITY SAFETY BUILDING

## Project Update



FMC Meeting  
April 1, 2025  
Lands and Facilities



# Agenda

1. Design Update
2. Construction Update



# Design Update

Current design in progress:

- Grading Plan
- Floor Plan
- Mechanical and Electrical Systems
- Preliminary Landscape Drawings
- Preliminary Plan Approval







Lobby Seating Area



Front Desk



Lobby Seating Area



Multi-Purpose Room

# Construction Update

Next steps in construction:

- Foundations – Below-grade Structure
- Building – Above-grade Structure
- Landscaping
- Furniture and Equipment
- Commissioning and Balancing/Testing

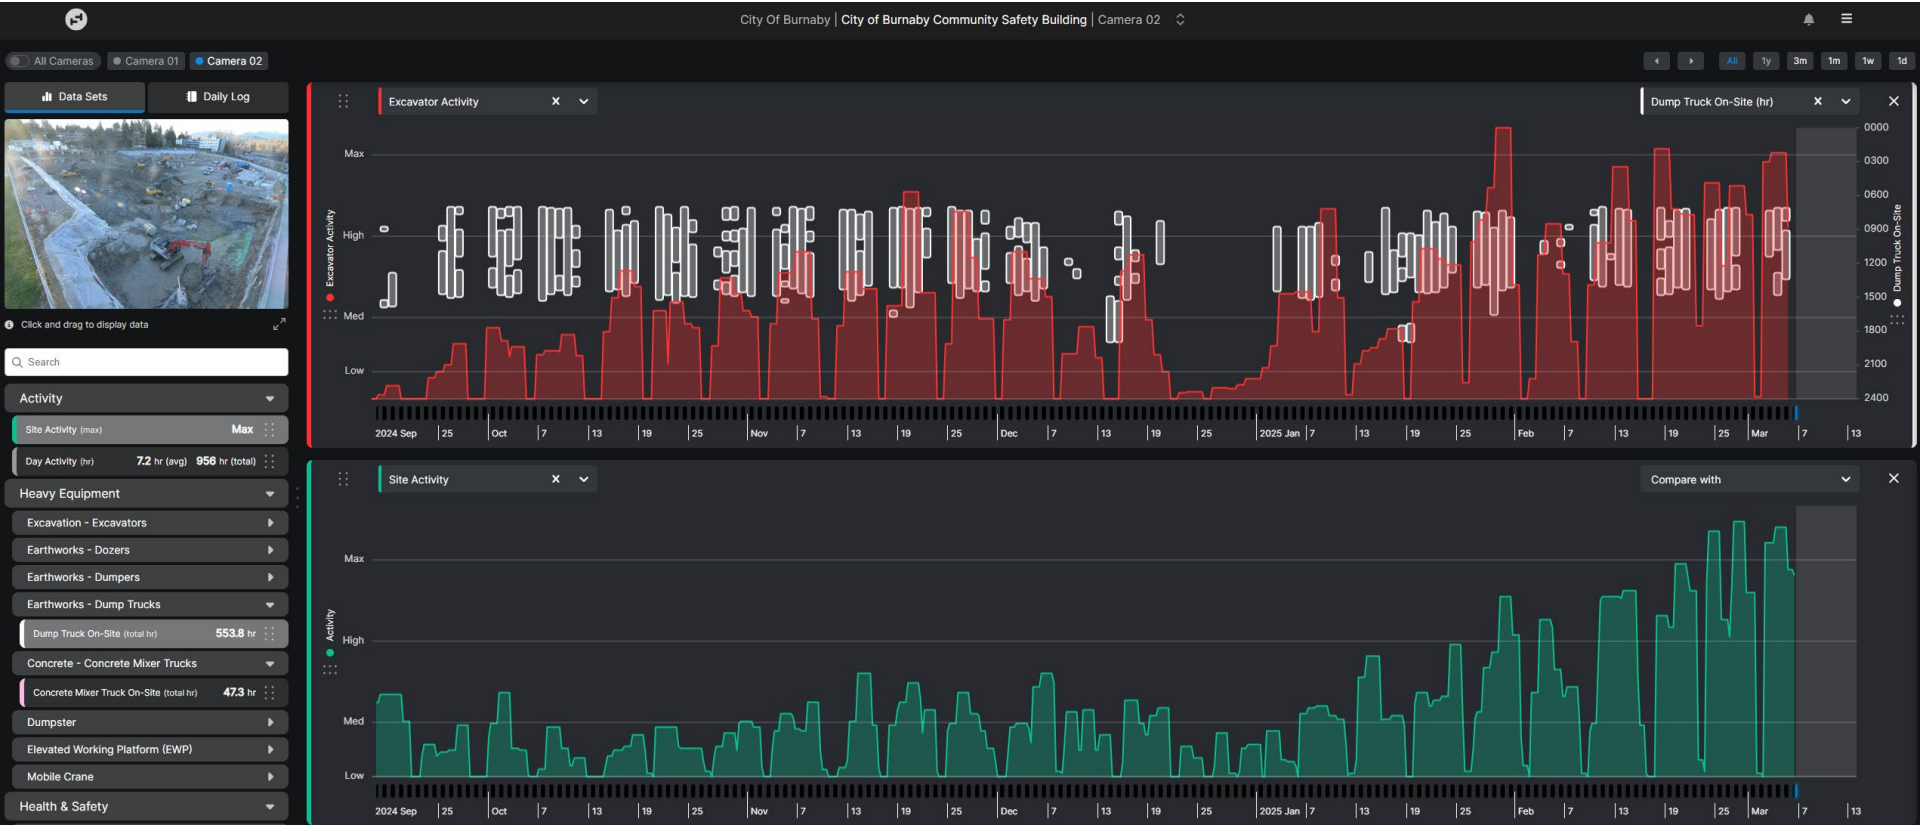




Photo taken February 26, 2025



# City Camera with Analytical Data







Site Excavation Activities  
February 2025



Sediment Erosion Control System with  
Real-Time Water Flow Monitoring



Truck Wheel Wash



Excavation and Shoring along the Western Property Line





Excavation of Underground Parkade






# Construction Update


Civic Project Schedules	2023				2024				2025				2026				2027				2028			
Project Name	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
RCMP Facility Replacement								11%																



## Community Safety Building

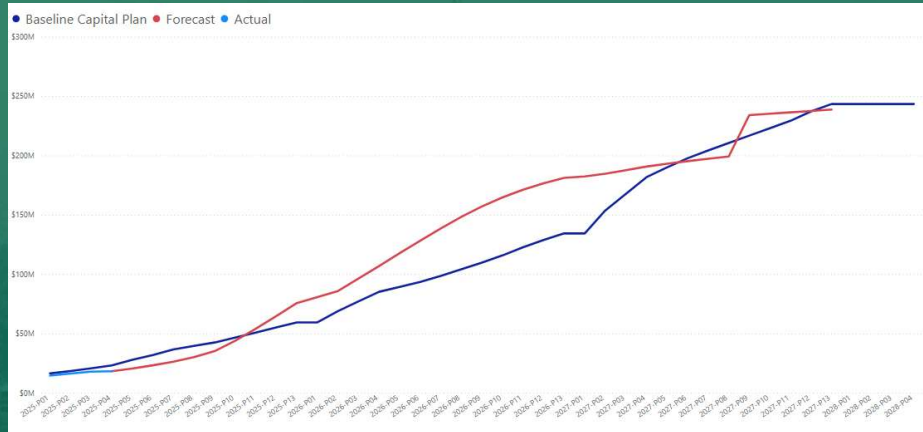

## Burnaby Lake Recreation Complex

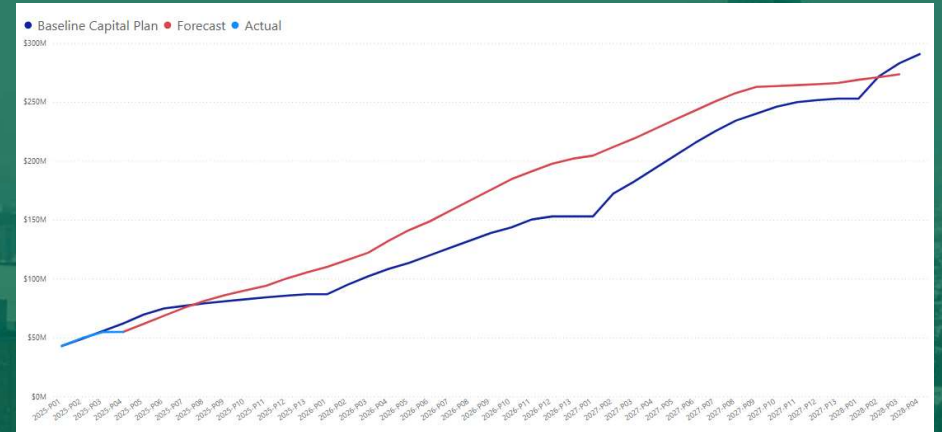

## James Cowan Theatre







# Questions?



# Fly Through Video
